


ID	Task Mode	Task Name	Duration	Start	Finish	11 April	01 June	21 July	11 Septem	01 Novem	21 Decemb	11 Februar	01
						31/03	21/04	02/05	23/06	04/07	04/08	05/09	06/10
1		Send out PE	0 days	Mon 28/04/14	Mon 28/04/14								
2		Companies prepare reply	4 wks	Mon 28/04/14	Fri 23/05/14								
3		Additional wait for replies if needed	1 wk	Mon 26/05/14	Fri 30/05/14								
4		Interpret replies, make DAI	2 wks	Mon 02/06/14	Fri 13/06/14								
5		Contract awarded	0 days	Fri 13/06/14	Fri 13/06/14								
6		Companies prepare purchasing plan	2 wks	Mon 16/06/14	Fri 27/06/14								
7		Delivery of purchasing plan	0 days	Fri 27/06/14	Fri 27/06/14								
8		Interpret purchasing plan	1 wk	Mon 30/06/14	Fri 04/07/14								
9		Approval by CERN of purchasing plan	0 days	Fri 04/07/14	Fri 04/07/14								
10		CERN items delivered to contractor	0 wks	Fri 04/07/14	Fri 04/07/14								
11		CERN delivers items on loan	0 days	Fri 22/08/14	Fri 22/08/14								
12		Production pre-series	12 wks	Mon 07/07/14	Fri 26/09/14								
13		Delivery of pre-series	0 days	Fri 26/09/14	Fri 26/09/14								
14		Testing pre-series by CERN	1 wk	Mon 29/09/14	Fri 03/10/14								
15		Acceptance by CERN of the pre-series	0 wks	Fri 03/10/14	Fri 03/10/14								
16		Production series	8 wks	Mon 06/10/14	Fri 28/11/14								
17		Delivery of series	0 days	Fri 28/11/14	Fri 28/11/14								
18		Testing series by CERN	2 wks	Mon 01/12/14	Fri 12/12/14								
19		Acceptance series by CERN	0 days	Fri 12/12/14	Fri 12/12/14								
20		Return of items loaned by CERN	0 wks	Fri 20/02/15	Fri 20/02/15								

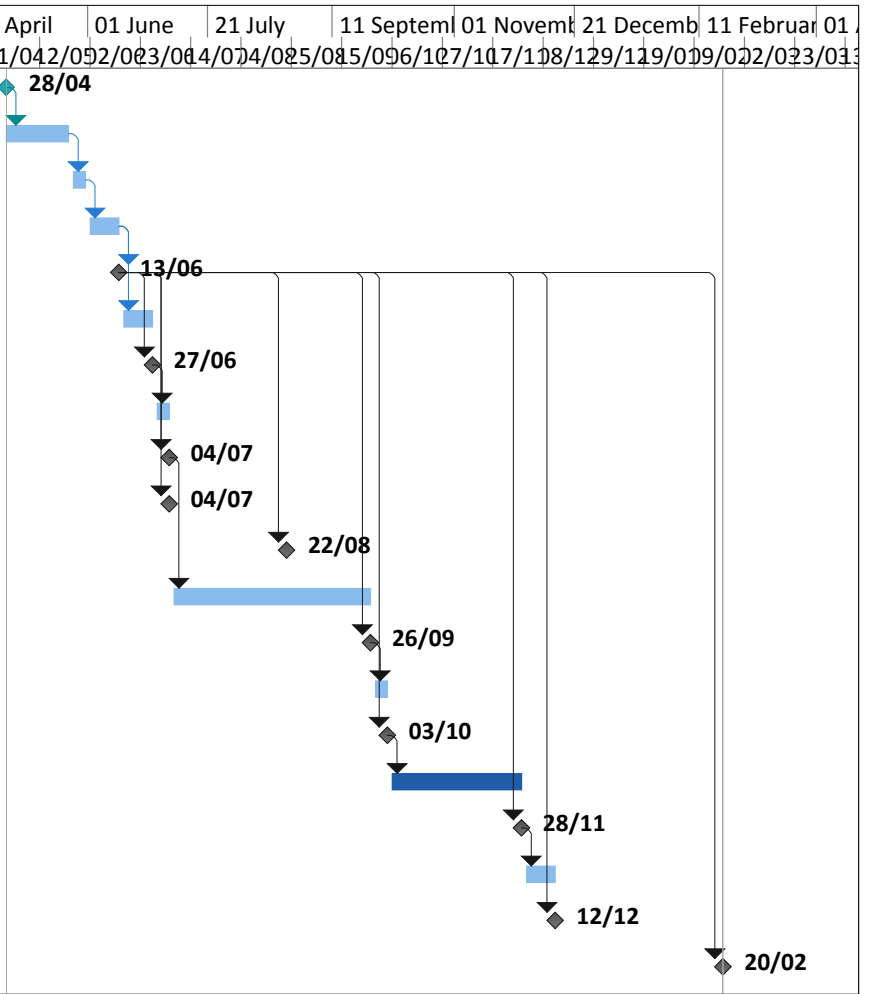

Project: Planning Date: Wed 18/11/15	Task		Inactive Task		Start-only	
	Split		Inactive Milestone		Finish-only	
	Milestone		Inactive Summary		Deadline	
	Summary		Manual Task		Progress	
	Project Summary		Duration-only		Manual Progress	
	External Tasks		Manual Summary Rollup			
	External Milestone		Manual Summary			
